



WORLD BANK GROUP



MISSION 300 COMPACT PROGRESS REPORT

SECOND CYCLE OF DATA COLLECTION 2025

 CHAD

MARCH 2026

Disclaimer: This report has been prepared and validated by the Government through its Compact Delivery and Monitoring Unit (CDMU). While Mission 300 partners support the reporting process and its standardization, responsibility for the content, data, and interpretations rests solely with the Government.

IN COLLABORATION WITH



Global Energy Alliance
for People and Planet
GEAPP

FOR
EXTERNAL
USE



DATA SOURCES AND DISCLAIMER

Under the **Mission 300 initiative**, progress on **National Energy Compacts** is monitored **twice a year** through data submitted by each country’s **Compact Delivery and Monitoring Unit (CDMU)**.

Monitoring covers both **policy reform actions** and **key targets** across four thematic areas:

- Electricity access
- Clean cooking access
- Share of renewable energy in national generation
- Private Capital mobilized

Countries report progress using a **standardized Excel template**, based on which **Compact Progress Reports (CPRs)** are produced. Each CPR is **prepared and validated by the Government through its CDMU**. While Mission 300 partners support the reporting process, **countries retain full ownership of data and responsibility of its interpretation**.

This report presents the **latest country-reported data**, submitted during the **Q1 2026 reporting cycle** and reflects **progress achieved in 2025**. The data provided is **country-reported and based on national methodologies**, which may limit direct comparisons across countries.

DEFINITIONS & METHODOLOGY

Priority Reform Action Status

- **NOT YET DUE:** No activities initiated for this action
- **IN PROGRESS – ON TRACK:** Implementation progressing well, no issues to be reported
- **IN PROGRESS – MINOR DELAYS:** In Progress but slight issues or minor delays expected
- **IN PROGRESS – AT RISK:** In Progress but major challenges, high risk of delay expected
- **DELAYED:** Deadlines passed and activities remain incomplete
- **COMPLETED:** All implementation activities concluded

“Connections” and “People Provided with Electricity access” Methodology

“**New electricity connections**” refers to additional electricity connections established since the start of Mission 300 up to the reporting year, across all solution types (grid, mini-grids, and solar home systems). To estimate the number of people gaining electricity access, the number of new connections is multiplied by the national average household size provided by the government (when available). This conversion is illustrative and does not imply that each connection corresponds to exactly one household.


GLOSSARY

AfDB African Development Bank	PSMP Power System Master Plan
CDMU Compact Delivery and Monitoring Unit	SEforALL Sustainable Energy for All
CPR Compact Progress Report	USD United States Dollar
GEA Global Energy Alliance	WBG World Bank Group
MTF Multi-Tier Framework (measuring energy access)	
M&E Monitoring and Evaluation	
NES National Electrification Strategy	

CHAD NATIONAL ENERGY COMPACT

Under the Mission 300 initiative, Chad presented its National Energy Compact in January 2025 at the Africa Energy Summit in Dar es Salaam, as part of the first cohort of twelve countries, outlining its reform commitments and targets to accelerate electricity access and mobilize private investment.

This Compact Progress Report tracks Chad’s progress against these commitments using data submitted by the Compact Delivery and Monitoring Unit (CDMU), with the latest update provided in January 2026.

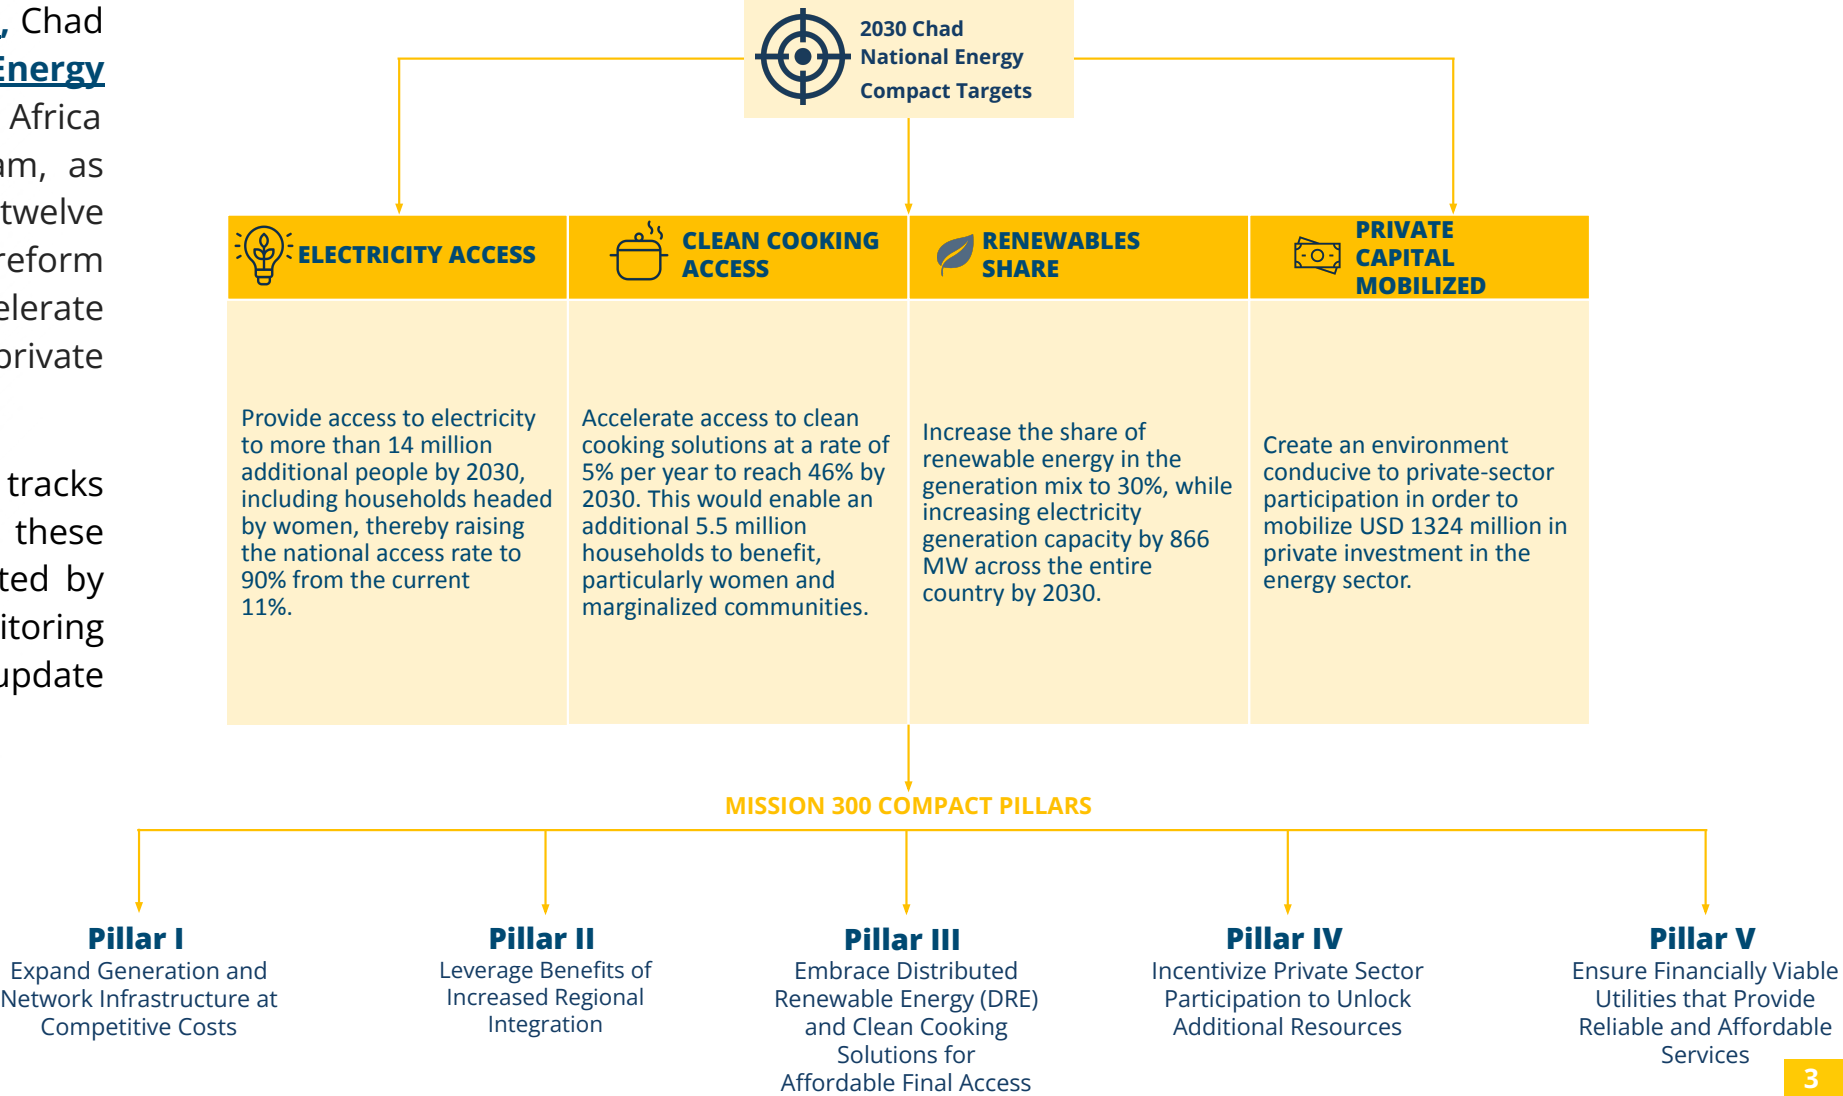

KEY TARGETS

The reporting period covers progress until 31 December 2025.

Chad has reported progress under its Energy Compact, particularly in electricity access, with **806,257 additional people connected** to electricity (subject to update in the next data collection cycle). The country is currently expecting additional data.

Clean cooking access has been extended to additional 24,274 people. A percentage of that representation the population is yet to be confirmed. The CDMU is awaiting additional data to determine.

Renewable energy represents 9% of national generation, compared to a 30% target by 2030. Multiple power generation systems were in 2025 which increased the percentage to 31%.

No private capital mobilized to date against the 2030 target of USD 1.324 Billion. The current figure for the mobilized capital may change following interest expressed as a result of the signature with the PASET II, the SMARTED for Clean Cooking, all within the framework of the Chad Connection Plan.

Quantitative data presented in this slide reflect the information available as of the latest reporting cycle provided by the Compact Delivery and Monitoring Unit (CDMU).

CHAD



CHAD'S PROGRESS ON HIGH-LEVEL COMPACT TARGETS			
Key Target	2023 Baseline	Progress to date (over 2025)	2030 Target
People with new Electricity Access (# of people ¹)	2,010,642	+806,257	+14,000,000
Clean Cooking (% of population)	10%	No data provided yet	46%
Share of Renewable Energy in national generation (% of generation)	9%	31%	30%
Private Capital Mobilized (million USD)	\$164	No data provided yet	\$1324

¹ “People with New Electricity Access” refers to the number of additional people with electricity access during the reporting year (2025), based on data submitted as of January 2026.

OVERVIEW OF REFORMS ACTIONS STATUS

CHAD 	PILLAR I	PILLAR II	PILLAR III	PILLAR IV	PILLAR V	Total	STATUS		
	Expand Generation and Network Infrastructure at Competitive Costs	Leverage Benefits of Increased Regional Integration	Embrace Distributed Renewable Energy and Clean Cooking Solutions for Affordable Final Access	Incentivize Private Sector Participation to Unlock Additional Resources	Ensure Financially Viable Utilities that Provide Reliable and Affordable Services		No of actions COMPLETED	No of actions IN PROGRESS**	No of actions DELAYED
Priority Actions	3*	1	3	1	2	10	0	9	1
Other Actions	0	1	1	1	1	4	2	2	0
Total	3	2	4	2	3	14	2	11	1

* One new priority action added (Under Pillar 1) by CDMU of Chad and not in original Compact.

** For the purposes of this table, all actions with an “In Progress” status are presented in aggregated form. In the original Priority Action reporting, this status is disaggregated into the following categories: (i) Not Yet Due; (ii) In Progress – On Track; (iii) In Progress – Minor Delays; and (iv) In Progress – At Risk. The disaggregated status by category is detailed when appropriate in the next slide.

Reform Actions

Chad’s National Energy Compact initially included thirteen (13) Reform Actions across the five (5) pillars. During the second cycle of data collection for the Compact Progress Reporting, one new priority action was introduced by the CDMU (highlighted in red in the next slide), bringing the total to 14 actions, of which 10 have been designated as Priority Reform Actions. Priority actions are subject to enhanced monitoring, while the remaining actions continue to be tracked by the CDMU.

By pillar, the distribution is as follows: Pillar I – 3 actions (3 priority); Pillar II – 2 actions (1 priority); Pillar III – 4 actions (3 priority); Pillar IV – 2 actions (1 priority); and Pillar V – 3 actions (2 priority).

As of December 2025, 2 actions (none of which are priority actions) are completed, 11 are in progress (including 9 priority actions) and 1 priority action is reported as delayed.



FOCUS ON PRIORITY REFORMS ACTIONS

Chad Energy Compact Priority Reform Actions						
#	Pillar	Commitment / Indicator	Priority Reform Actions	Deadline	Current Status	Previous Status
1	Pillar I - Expand Generation and Network Infrastructure at Competitive Costs	Integrated least-cost power system planning adopted incorporating regional resources	Finalize and adopt the comprehensive Power System Master Plan (PSMP)/Integrated Resource Plan	31-Mar-26	In-Progress On track	N/A
2		Competitive procurement policy and framework in place for private-sector investment in renewable energy	Framework set out for competitive procurement procedures	30-Jun-26	In-Progress On track	N/A
3		Review of the renewable energy master plan	Develop a master plan for the deployment of renewable energy, specifically covering the investment programme as well as the financial and economic analysis, based on current and future demand and the potential supply of renewable energy across the 23 regions of Chad*	31-Oct-26	In-Progress On track	N/A
4	Pillar II - Leverage Benefits of Increased Regional Integration	Adopt and enforce harmonized transmission pricing within the respective power pools to facilitate the power trade across borders	Develop and adopt transparent and standardized and Transmission Pricing Methodology aligned with regional standards	31-Dec-27	In-Progress On track	N/A
5	Pillar III - Embrace Distributed Renewable Energy and Clean Cooking Solutions for Affordable Final Access	Monitoring and evaluation program adopted to track the MTF for access to electricity and clean cooking	The Emergency Plan for Access to Electricity developed in 2020 provided for the establishment of a M&E mechanism for the sector, including tariff adjustments	31-Dec-25	Delayed	N/A
6		National Electrification Strategy (NES) adopted including an updated five-year electrification plan with a clearly defined role for private sector	Update and approve the NES	31-Dec-26	In-Progress On track	N/A
7		National clean cooking strategy in place	Update the Clean Cooking Strategy	30-Jun-26	In-Progress On track	N/A
8	Pillar IV - Incentivize Private Sector Participation to Unlock Additional Resources	Process outlined for regulatory approval of private-sector-led mini-grids (including tariff regulations)	Implementation of Law 036/19 on the Electricity Sector provides for the regulation of off-grid solutions	30-Jun-26	In-Progress On track	N/A
9	Pillar V - Ensure Financially Viable Utilities that Provide Reliable and Affordable Services	Audited annual financial statements of utilities published	Disclose the audited financial statements after the financial year (FY) close	30-Jun-26	In-Progress On track	N/A
10		Utilities achieving at least 100 percent operational cost recovery	Achieve 100% of recovery rate	31-Dec-28	In-Progress On track	N/A



ABOUT MISSION 300

Mission 300 is a joint initiative by the World Bank Group and the African Development Bank (AfDB), supported by The Rockefeller Foundation, SEforALL, GEAPP, which aims to provide electricity access to 300 million Africans by 2030. This ambitious goal seeks to halve the current number of people without electricity on the continent, driving sustainable development through collaboration and innovative solutions

IN COLLABORATION WITH



Global Energy Alliance
for People and Planet
GEAPP

